



# Community Construction Update

Edition#2

## Narcoossee Road Construction

Orlando Mayor Buddy Dyer is committed to keeping residents and businesses updated on the Narcoossee Road Improvement project. This Community Construction Update has been created by the City to provide the most current information on the project.

### Project Highlights

- Four-lane road with sidewalks, drainage and streetlights
- City of Orlando sanitary sewer system
- Orange County Utilities reclaimed water line

### Project Status

- Prince Construction has completed 71% of the construction work.

### Completed Work

- Stormwater drainage systems
- New underground utilities: sanitary sewer gravity system, reclaimed water line
- Relocated underground utilities: natural gas line and telecommunication cables
- Driveways, sidewalks and curbs along the southbound west side roadway
- Medians and base course of asphalt pavement
- Northbound traffic south of the Beachline Expressway (S.R. 528) switched to new lanes

### Upcoming Work

### Time Frames

- Streetlights installed along west side of Narcoossee .....Installation Complete
- Paving of Narcoossee southbound lanes between Leevista Boulevard and McCoy Road .....Complete
- Paving of Narcoossee north of Leevista Boulevard .....Complete
- Work finishes on Beachline Expressway ramps .....Complete
- Traffic shifted to permanent pattern of divided highway with median openings -  
One northbound lane on east and one southbound lane on west  
Work continues in middle of roadway - temporary median crossovers are closed .....Complete
- Milling and resurfacing Leevista Boulevard - Two Phases .....Phase 2 end of March
- Grass sod installed in medians .....In Progress
- Four lanes open to traffic - occasional temporary lane closures .....Early April
- Sanitary sewer lift station completed .....Mid April
- Project is substantially complete - clean up and adjustments may continue .....End of April

*Time frames may change due to adverse weather, delayed material deliveries, unforeseen events, or site conditions*

Prince Contracting, LLC , and the City of Orlando appreciate your continued cooperation and patience during the remainder of the work.

### Contact Information

Public Information: Quest Corporation of America  
Karen Kersey – 407.709.9840


Construction and Daily Work Program: Wilbur Smith Associates  
Elizabeth Ray – 407.273.0552

Sanitary Sewer System(New Connections): City of Orlando Wastewater Division  
Chuck Shultz – 407.246.2658

Project Manager: City of Orlando  
Ben Gray – 407.246.2754



# Narcoossee Road Construction Progress

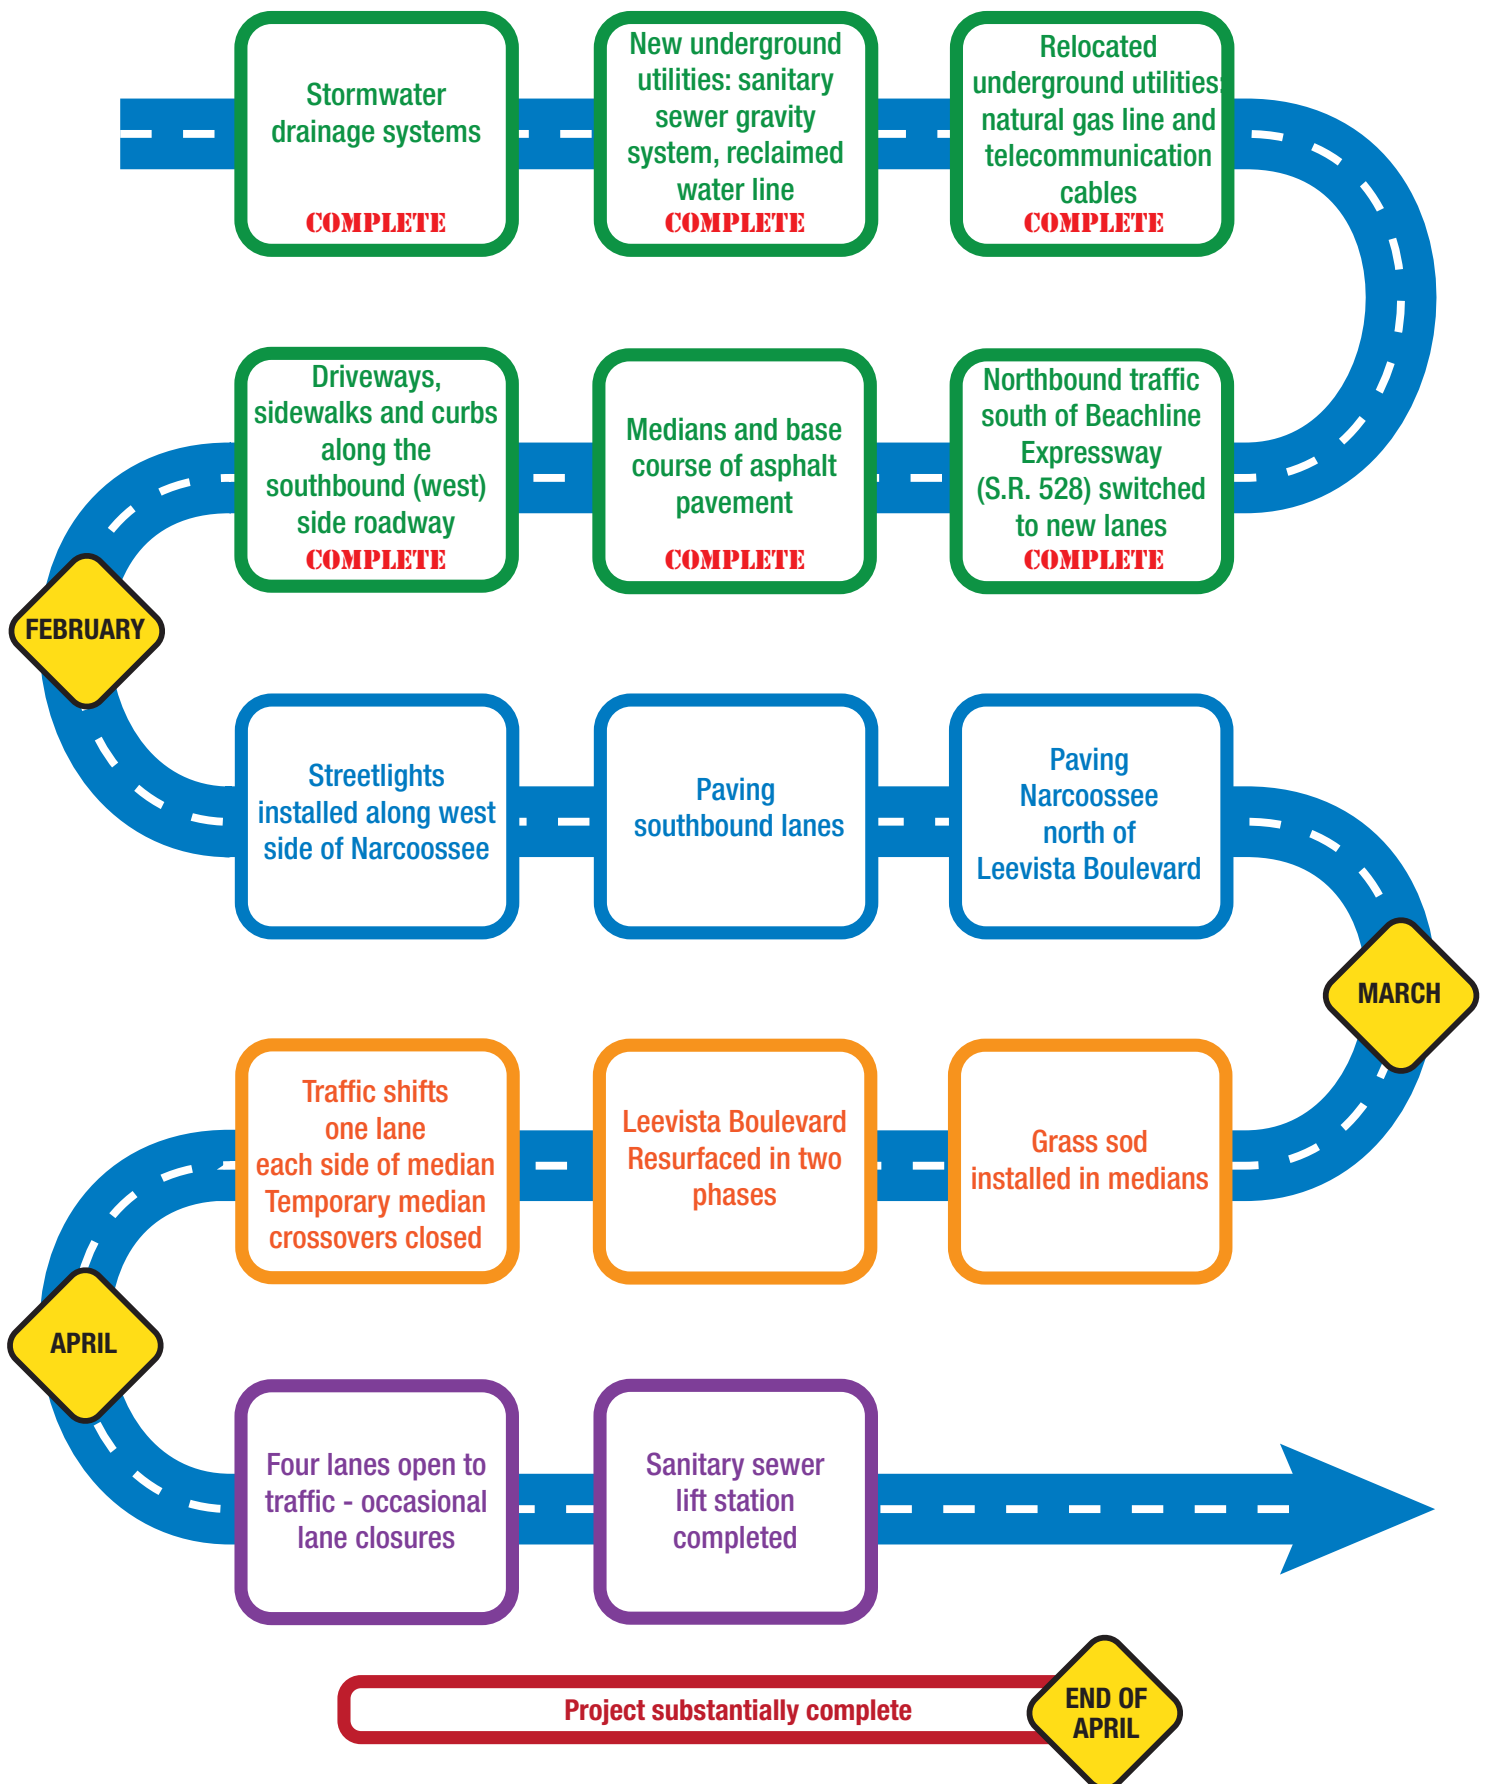

*Time frames may change due to adverse weather, delayed material deliveries, unforeseen events, or site conditions*
